Month 3 progress report

Baakhapaa: AI-powered pre-production intelligence system Weeks 9 to 12 of 12 · Prepared for Baakhapaa · Reference: proposal §8

The three items Month 2 named as blocking everything else were strictly ordered, and the first two are done. A cloud database was created and its migrations applied; the application was deployed on 15 September and has been running since. The third — merchant applications to Khalti and eSewa — is not a build task and has not moved.

161 of 200 planned tasks are complete. The honest shape of the remaining 39 is the most useful thing in this report: **29 of them are not work.** They are purchases and a person holding a phone. No amount of engineering moves them, and the month ends with the product built and a specific, short list of things that must be bought before it can be proven.

The month's second result is less comfortable. Half the commits answered no checkbox on the plan, because **ten defects were found that were on no list at all** — six of them invisible to the test suite as it then stood. That distribution is itself a finding, and section 6 treats it as one.

1. What the month produced

Planned tasks complete	161 of 200
Remaining tasks blocked on a purchase or a person	29 of 39
Commits	150
Suite size	1,146 backend tests in 75 files; 1,281 frontend tests in 66 files
Defects found that were on no plan	10, of which 6 were invisible to the suite
Retrieval, real queries	**91.3%** combined, **90.0%** screenplay, measured this week
Deployed	15 September, Vercel + Railway + Supabase
Real money moved	None

2. The proposal's three blocking items

A cloud database, migrations applied — done. The email-normalisation migration ran first and alone, as planned, because it was the only one that could fail on existing data. The others followed. Two migrations are applied by hand in the SQL editor and a new Supabase project would still need them; `check_schema.py` now asks the real database whether each table matches what the code writes, so this is answered by the database rather than by a document. That check caught a claim in our own notes that a table was unapplied when it had existed for weeks.

Deployment — done, 15 September. It exercised the production configuration checks for the first time, which is what they were written for: the backend refuses to start on an unset origin list, a demonstration account left enabled, a local database file, or a Devanagari font resolving only to the non-redistributable one. Register, login, project creation, draft save, cast, lint, recommendations and review all return 200 against the deployed pair. Scene sync reconciled a Devanagari draft in production Postgres.

Three environment-variable traps cost an hour between them and are written down in `DEPLOYMENT.md` so they cost nobody else one.

Merchant applications — not started. Both require company registration and a business bank account alongside the live URL. This is the item the proposal correctly identified as depending on somebody else's calendar.

3. What a writer can do today, and what it costs

The product has two halves, and only one of them needs money to run.

The free half works and was the month's main beneficiary. The craft linter, the Patterns tab, the coverage report, the corpus benchmark, the nineteen-lesson course and all four exports run with **no AI call at all**. They work on a half-written draft, cost nothing per use, and give the same answer twice.

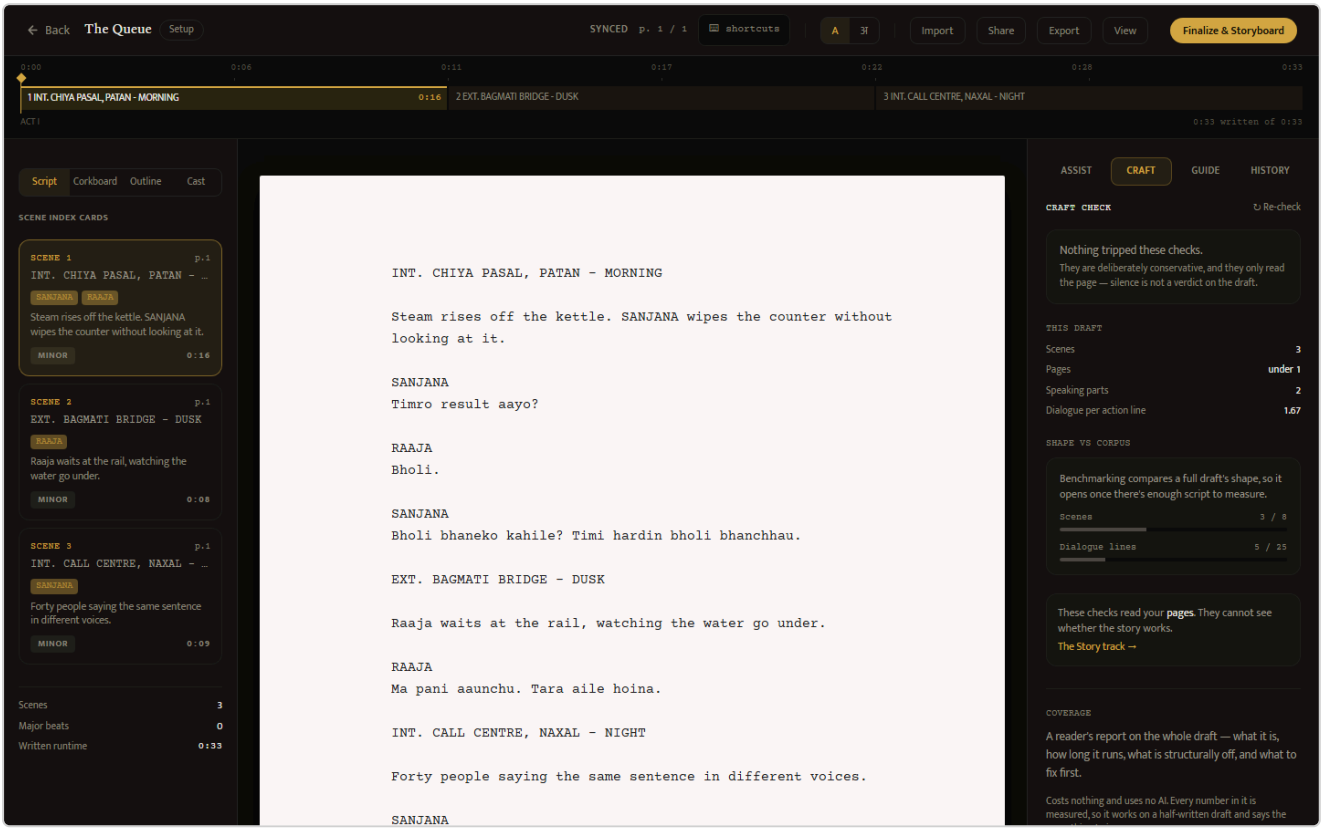


Figure 1 — the linter, the draft's own statistics and the corpus benchmark. Every number here is counted, not generated. Nothing in this view makes a paid API call.

Retrieval became diagnosis-first this month: rather than answering a complaint the writer types, it reads the draft, names what it found and anchors each craft entry to a line.

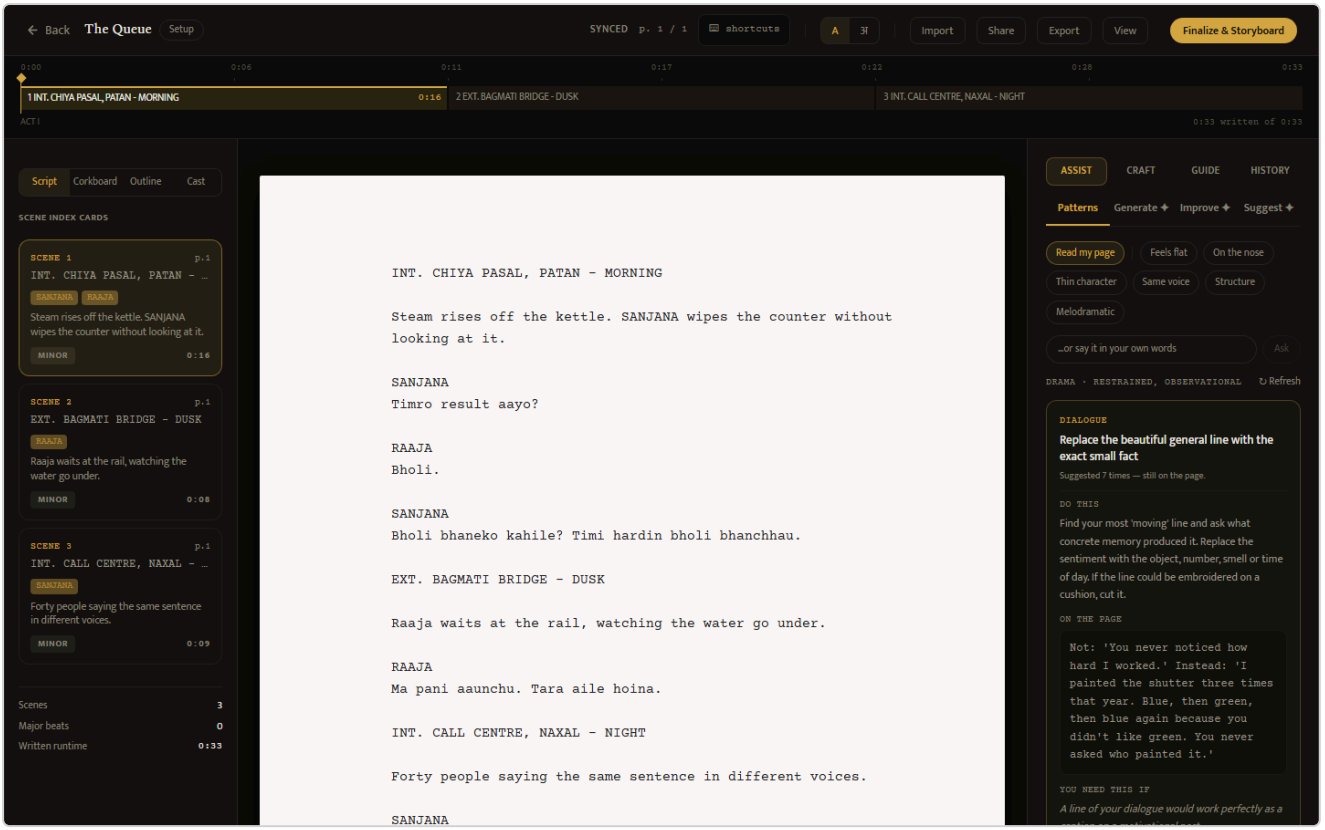


Figure 2 — craft retrieved from what is on the page. "Suggested 5 times — still on the page" is the recommendation log, which exists so the same three cards stop reappearing after a writer has acted on them.

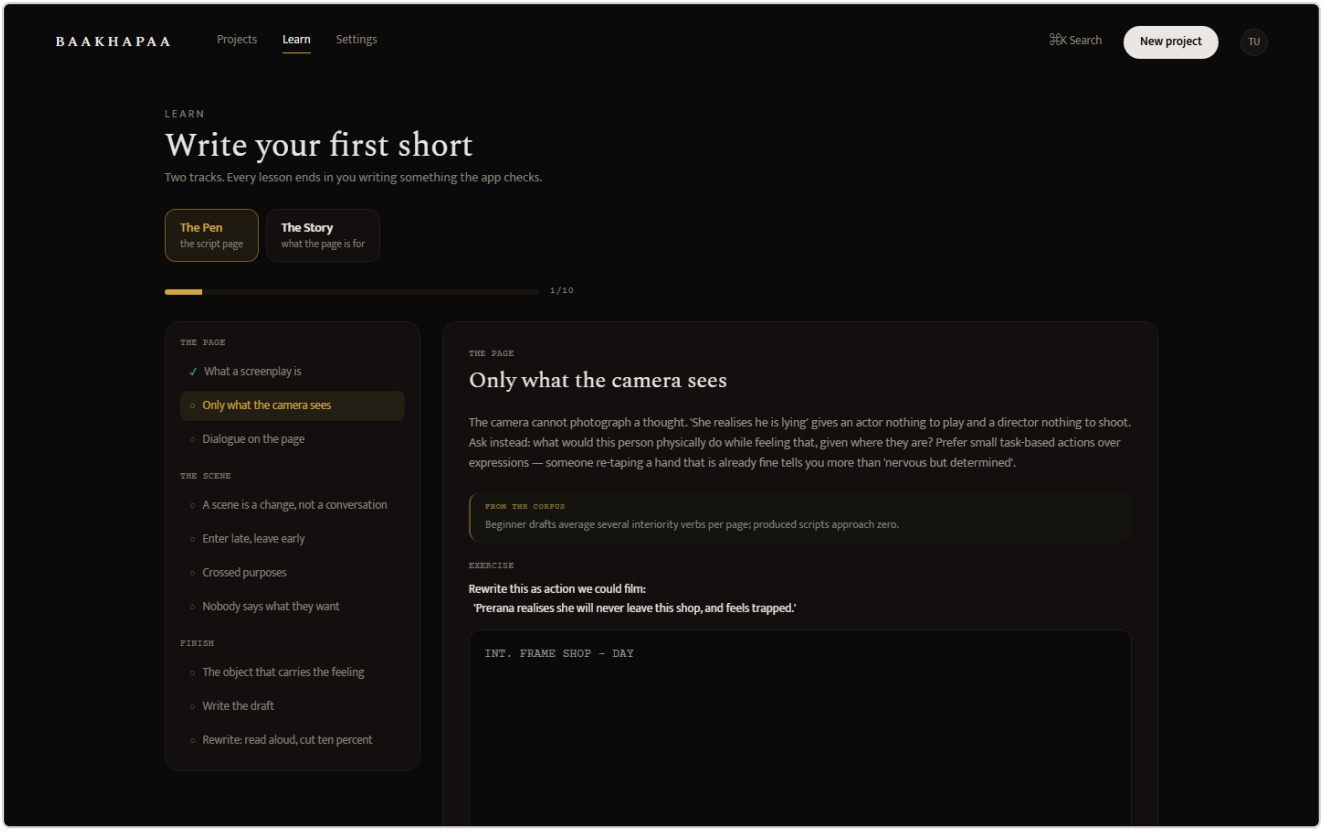


Figure 3 — nineteen lessons in two tracks, free on every tier, each graded by the craft linter rather than by a Next button. Verified working this month in both English and Nepali, in both directions: a correct answer passes, and a wrong one is refused with specific reasons.

4. The measurement the product is built around

Month 2 reported retrieval ranking the correct technique first in **20%** of real queries, and said that number mattered more than the flattering 82.4% that preceded it.

Measured again this week, on a golden set widened from 25 queries to 46:

	n	precision@1
Combined	46	**91.3%**
Screenplay only	40	**90.0%**
Long-form video	6	100%
Devanagari queries	6	83.3%
Romanised Nepali	13	84.6%

Two things made the difference, and one of them is a negative result worth more than the gain.

A Nepali complaint is now translated out of Nepali before it is embedded. A Devanagari query scored 16.7% — the product's differentiator working worst for the market it exists for. The obvious fix was a Nepali gloss field in the corpus. **Measurement killed it:** the embedding model scores two Devanagari sentences at 0.898 same-meaning against 0.877 different-meaning, a gap of 0.02. It cannot read the script at all, and a gloss field would have been work that looked like a fix.

CI now holds two floors rather than one. Averaging a weak new craft into a single number is exactly how an 82% headline once sat on top of a 20% reality. Screenplay keeps its own floor at 0.85, so the combined figure cannot hide a regression in the thing most users do.

A second negative result was recorded in full: adding image-level corpus entries to lift image-craft retrieval changed precision from 71% to 71% and *dropped* the sanity check from 100% to 91.8%. All four entries were reverted and the suggestion marked **"tested, and it does not work — do not retry it."** The cause is that writers describe image problems in scene and character vocabulary, so it is a query-side problem, not a corpus-size one.

5. The change that most affects how the product is used

AI generation was gated on the subscription tier alone. A writer on a paid plan could open an empty editor and have a model write the first scene — the one thing this product argues against, and the reason structure generation was taken out of the creation wizard in Month 2.

The AI now opens on a finished first draft.

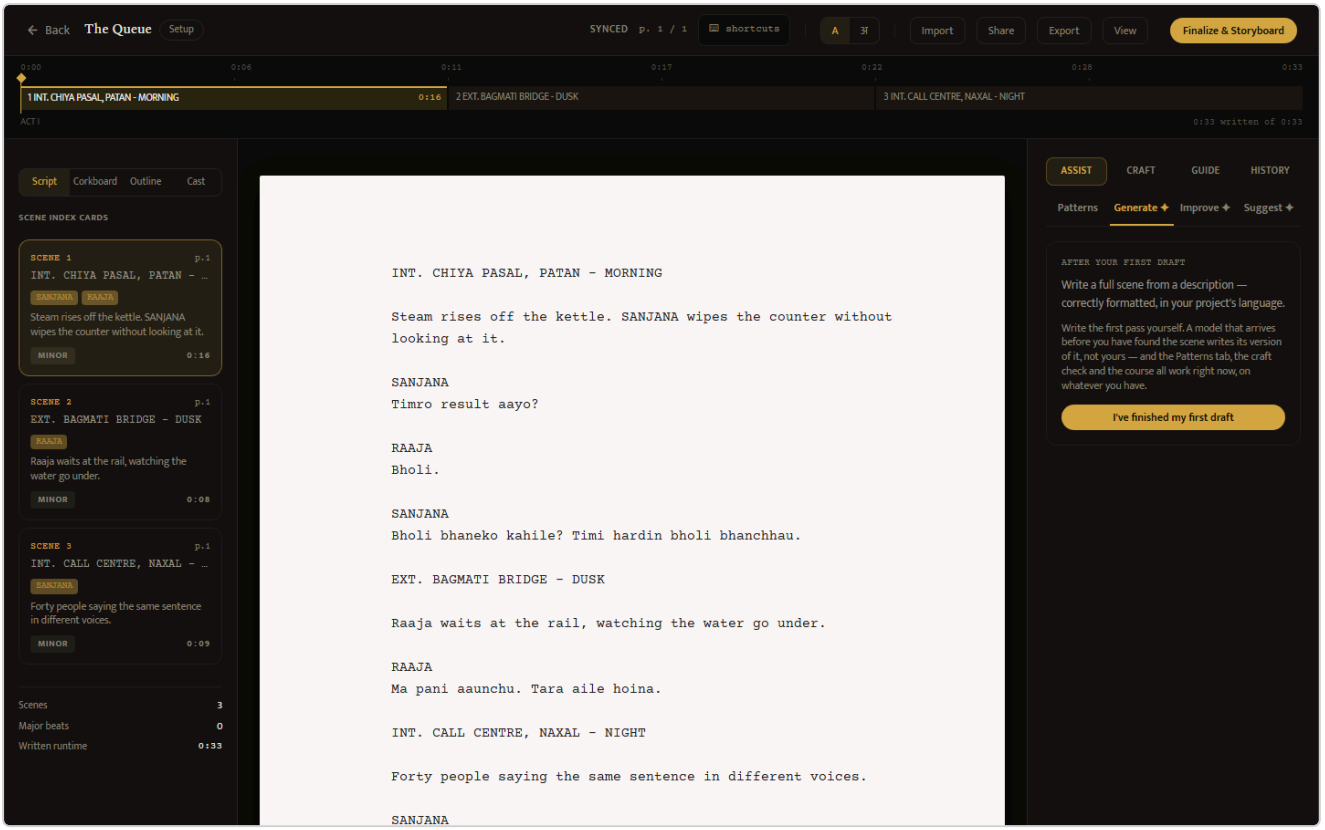


Figure 4 — the Generate tab before a draft is declared complete. It states the argument rather than refusing, and names what already works.

Three decisions inside it are worth recording:

It is a **declaration, not a measurement**. Nothing reads the draft and judges whether it is good — the linter does that, and it reports rather than judges. Writing more afterwards does not take the unlock away, because re-locking a writer mid-session over a word count would be the tool overruling the person. The only refusal is an empty page.

A free writer never meets this gate. Telling somebody to finish their draft when a paywall waits behind it would be a promise the product cannot keep. Tier and draft are separate locks and each writer is shown only the one that is actually theirs.

Every script that exists carries the old status, so on deploy each paid writer meets this once and presses one button. That was preferred to grandfathering, which would have made the rule mean different things for old work and new.

6. The ten defects, and why they matter more than the count

Roughly half of the month's 150 commits answer no checkbox on the plan. That is not drift: ten defects were found that were on no list, and **six were invisible to the test suite as it then stood.**

Three causes, each now closed:

The local test database is schemaless. It accepted columns Postgres would reject, so a missing column passed every test and broke *every project creation* in production. `check_schema.py` now asks the real database.

No test in this repository can see a layout. `vite.config.js` disables CSS in the test environment, so jsdom renders every component with no stylesheet. Every responsive defect found so far was found by a person on a phone, past a green suite. Three browser-based checks now run in CI that no unit test can perform.

A passing suite proves the code agrees with itself. Two faults this month were the suite making live, billed API calls, and the suite running against the production database. Neither failed; one hung for 75 minutes. A guard now stops the run outright rather than neutralising providers by name.

Two defects are worth naming individually.

A failed AI call offered to overwrite the draft. The error text was written into the same state the Accept button inserts into the page, so the panel rendered a green Accept under the provider's error. On a scoped rewrite, pressing it replaced the writer's highlighted lines with `Error: Request timed out`, and autosave persisted it a second later. Found by running the product with both providers down, which is the state it is in today.

The text caret measured 2.30:1 against the page, under the 3:1 floor, on a page whose body text runs at 15.81:1 — the one element a writer looks at for hours was the faintest thing on it. The contrast checker could not have caught it: its rule matched `color:` but not `caret-color:`. It now checks both.

7. Testing

	Month 2	Month 3
Backend tests	765 in 42 files	**1,146 in 75 files**
Frontend tests	1,020 in 54 files	**1,281 in 66 files**

Three things changed about how tests are trusted, not just how many there are.

The numbers in our own documentation are now counted, not typed. Four documents were wrong at once in September because every figure in them had been written by hand. `check_docs.py` derives them and fails CI on drift. The figures in this report came from it.

Tests are now checked for whether they can fail. Several tests written this month passed while the feature they covered was entirely inert — they asserted on canned data and read their own fixtures back. The practice now is to break the implementation deliberately, confirm the tests fail, restore, and record both results. Two features that looked finished and did nothing were caught this way.

The backend suite went from twenty minutes to twenty-eight seconds. The cause was password hashing across 754 user creations, not any individual slow test.

8. What is not done

Four things are built, tested, and have never run. None is waiting on further engineering.

	Waiting on
AI scene generation and improve	Paid API credit
Storyboard image generation	Paid image credit
A completed customer payment	Merchant accounts with Khalti and eSewa
Renewal reminder emails	An email sending account

The distinction that should run through any reading of this report is **built** against **proven**. Every planned feature exists. A smaller set has been demonstrated end to end.

Confirmed this week with live probes rather than assumed: Anthropic returns *"credit balance is too low"* and the development router returns *"no available channel"*. Every AI call in the product currently lands in a failure path — which is why the defect in section 6 was reachable by an ordinary user rather than theoretical.

Cost, when credit is bought. A scene improve is roughly one cent at current rates; the five-writer pilot fits inside a few dollars. The obstacle has never been the amount. It is that Anthropic bills through Stripe, which is the same rail that cannot collect from most Nepali cards — the reason this product supports Khalti and eSewa at all.

9. Month 4

Buy the four things. They are cheap, they are the only blockers, and three of the four unblock a deliverable the proposal names. Enabling international transactions on a Nepali card is the single highest-value hour available.

Run the pilot. `PILOT.md` holds the protocol: what only a writer can settle, what to measure rather than ask, and what counts as a failure. The proposal's success measure — one script completed without falling back to manual methods — is demonstrated or disproved there and nowhere else.

Then the two decisions building cannot settle. Whether Rs 999 holds against a market anchored nearer Rs 499, and whether launch is invitation-only. Both were raised in Month 2 and both are still open, because neither is a feature.

10. Decisions that cannot be settled by building

Three of Month 2's four remain open and unchanged: the price, the launch shape, and encryption of script text.

The legal documents still require a Nepal-qualified lawyer. This is the item that cannot be compressed by working harder. It has now been open for two months.

Figures were captured from the running system with `baakhapaa-frontend/scripts/capture-screenshots.mjs`, which the report runs rather than reproducing by hand — the Month 1 figures survived

into the Month 2 report once because they were recaptured manually and nobody noticed the editor had changed underneath them.

Test and corpus counts were derived by `baakhapaa-backend/check_docs.py`. Retrieval figures were produced by `eval_retrieval.py` against the live corpus on 2 October 2026.
